



# Road Project Status

JULY 22, 2015

**Joe Vidunas**  
**Dept. of Public Works**

# 1 – U.S. Rt. 360 (Bridge Replacement) COMPLETE



## 2 – Sliding Hill Rd / Air Park Rd Turn Lanes

Construction Phase – Aug. 2015 Completion Date




# 3 – Taylorsville Rd (Replace Bridge & Approaches)

**COMPLETE**



# 4 – U.S. Rt. 360 & Elm Dr. (Traffic Signal Upgrade)

## COMPLETE

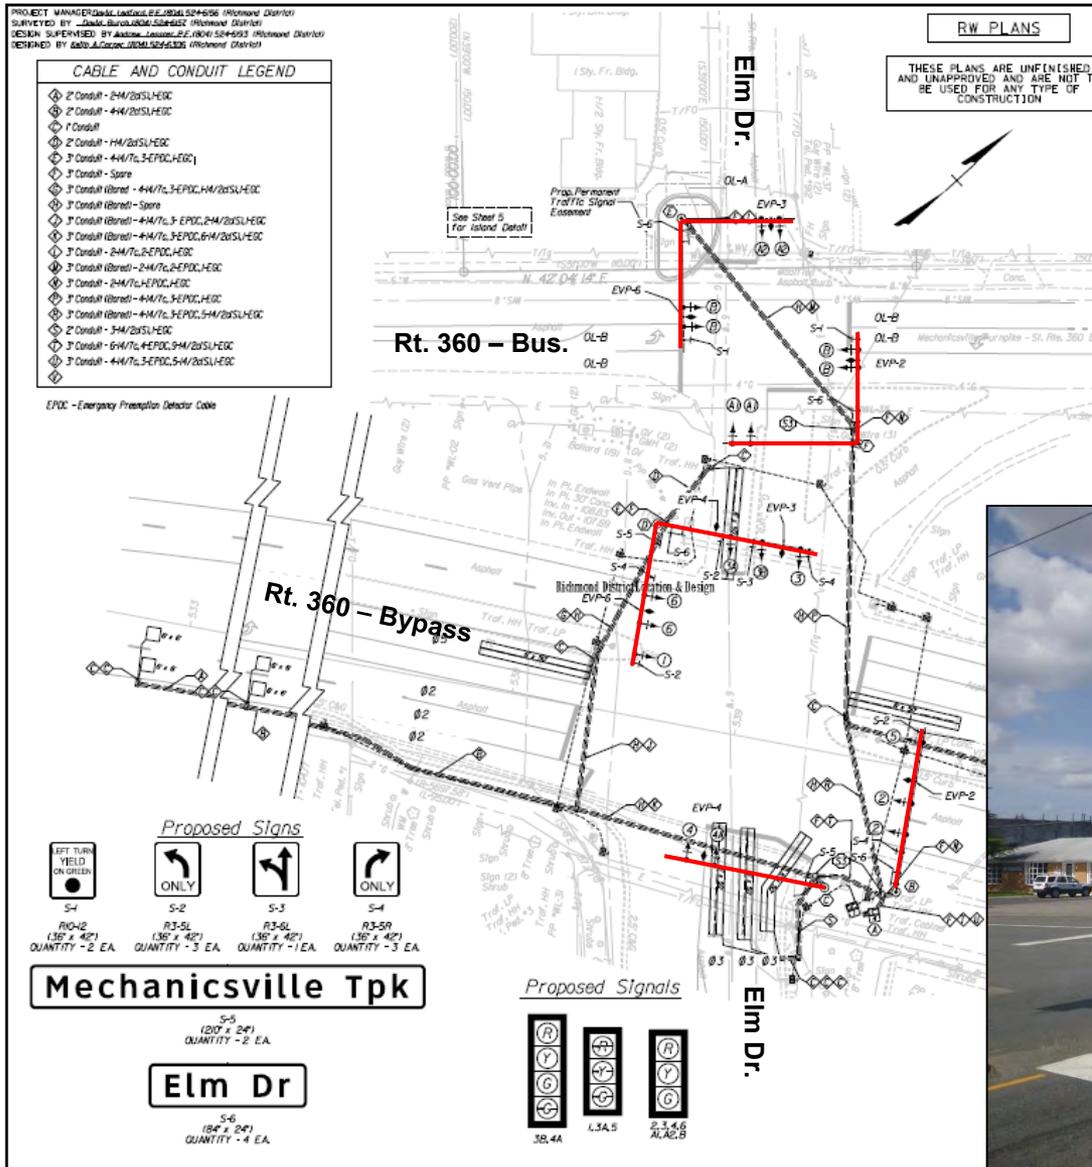

# 5 & 6 – U.S. Rt. 360 (I-295 – Wynbrook Ln)

PHASE 1 – Construction Phase – May '17 Completion Date




# 7 – I-95 / Lewistown Rd. (Bridge & Approaches)

## Construction Phase – Nov. '17 Completion Date





# 8 – Cool Spring Rd (Safety Improvements)

Pre-construction Phase – Sept. 2015 Begin Date

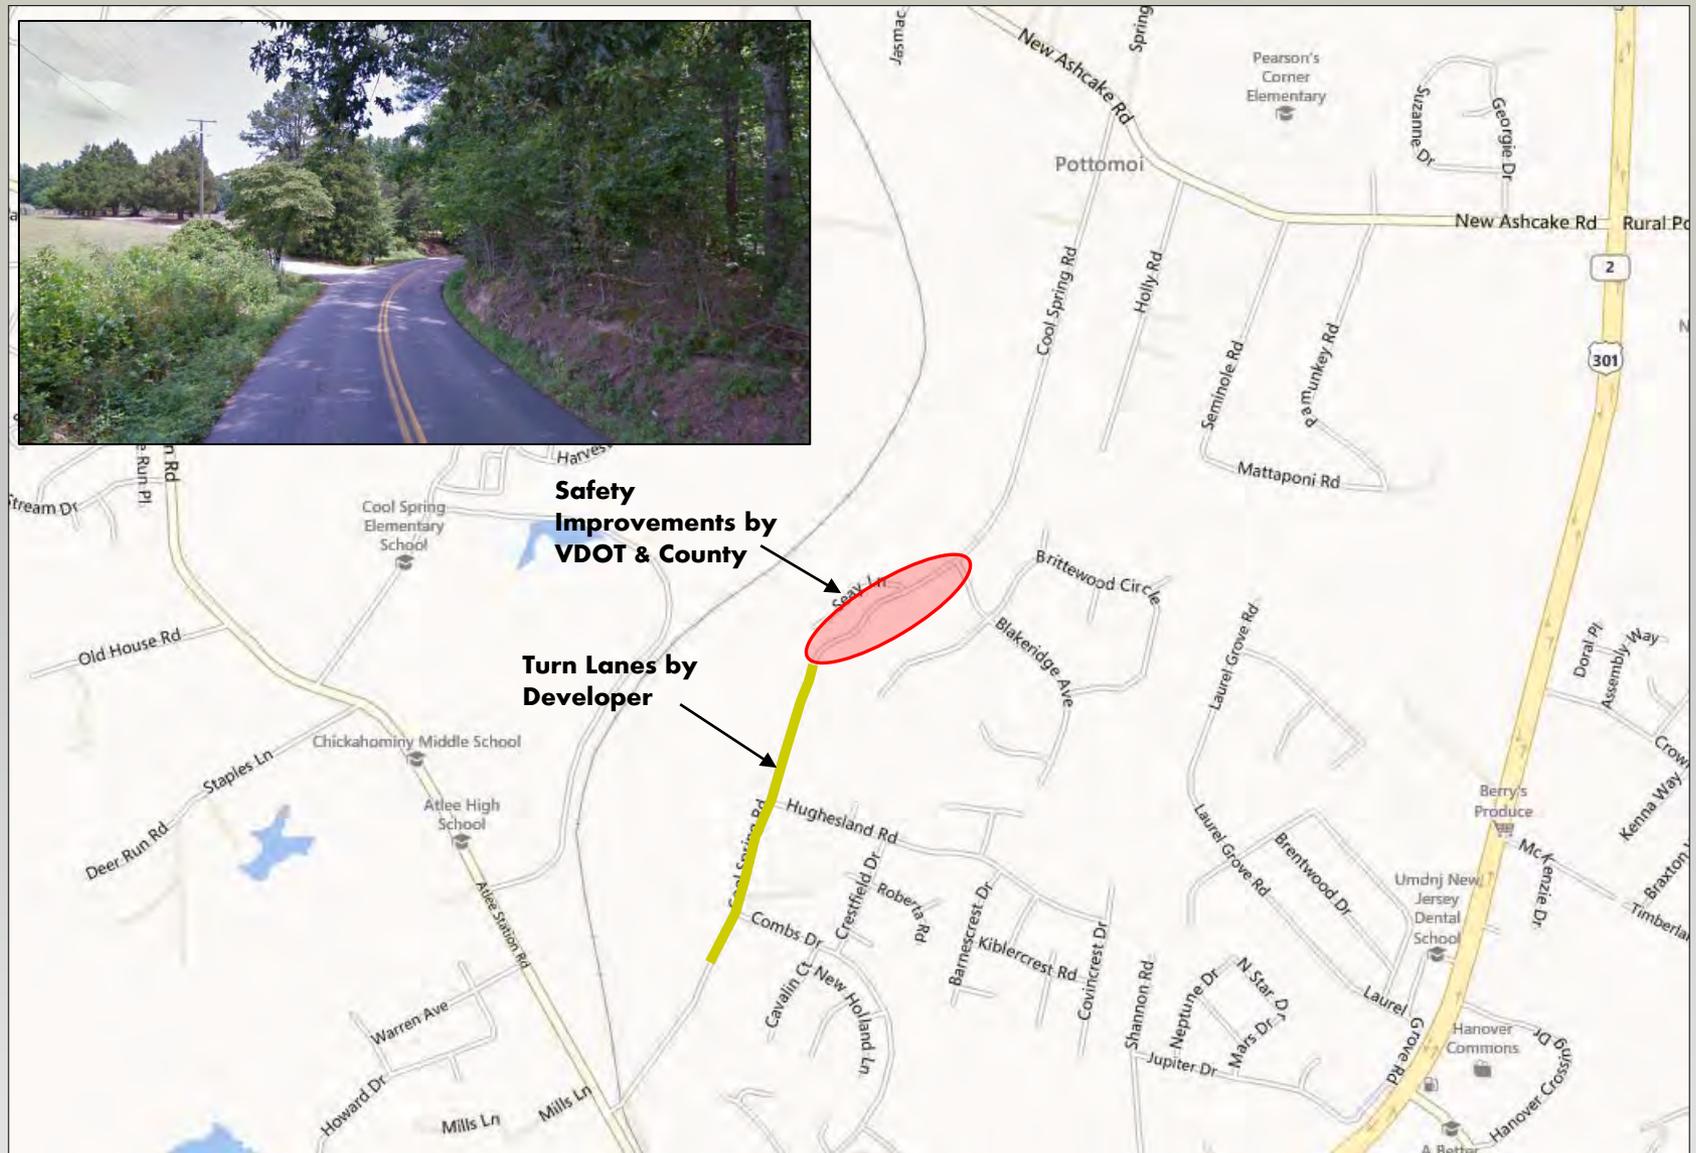

# 9 – Ashcake Rd (Trench Widen & Overlay)

## Advertisement Phase – Bids Due July 22

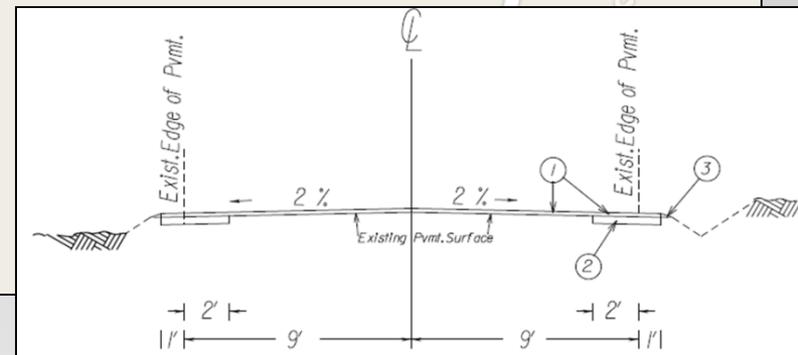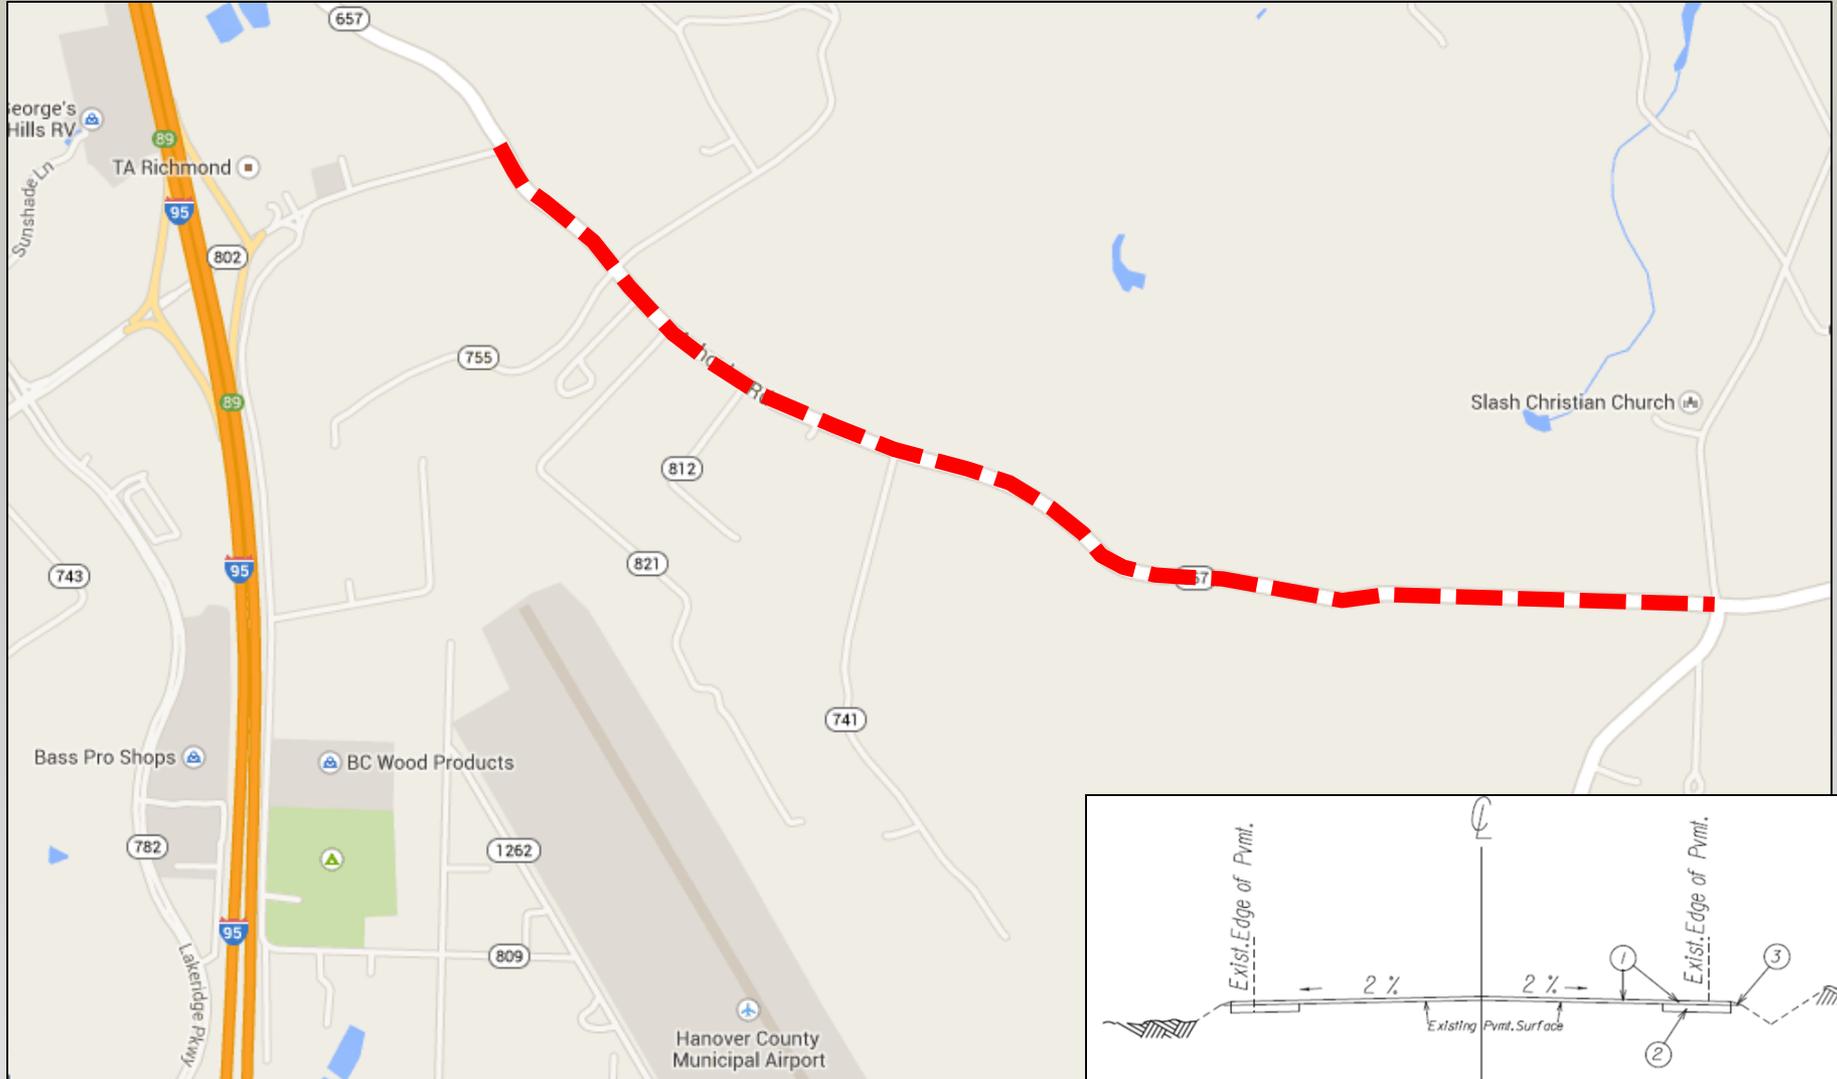




# 11 – Pole Green Rd / Walnut Grove Rd (Turn Lanes)

Utility Relocation Phase – Sept. 2015 Ad Date




# 12 – U.S. Rt. 33 / Ashland Rd (Turn Lanes)

## Right-of-Way Phase – Aug. 2016 Ad Date

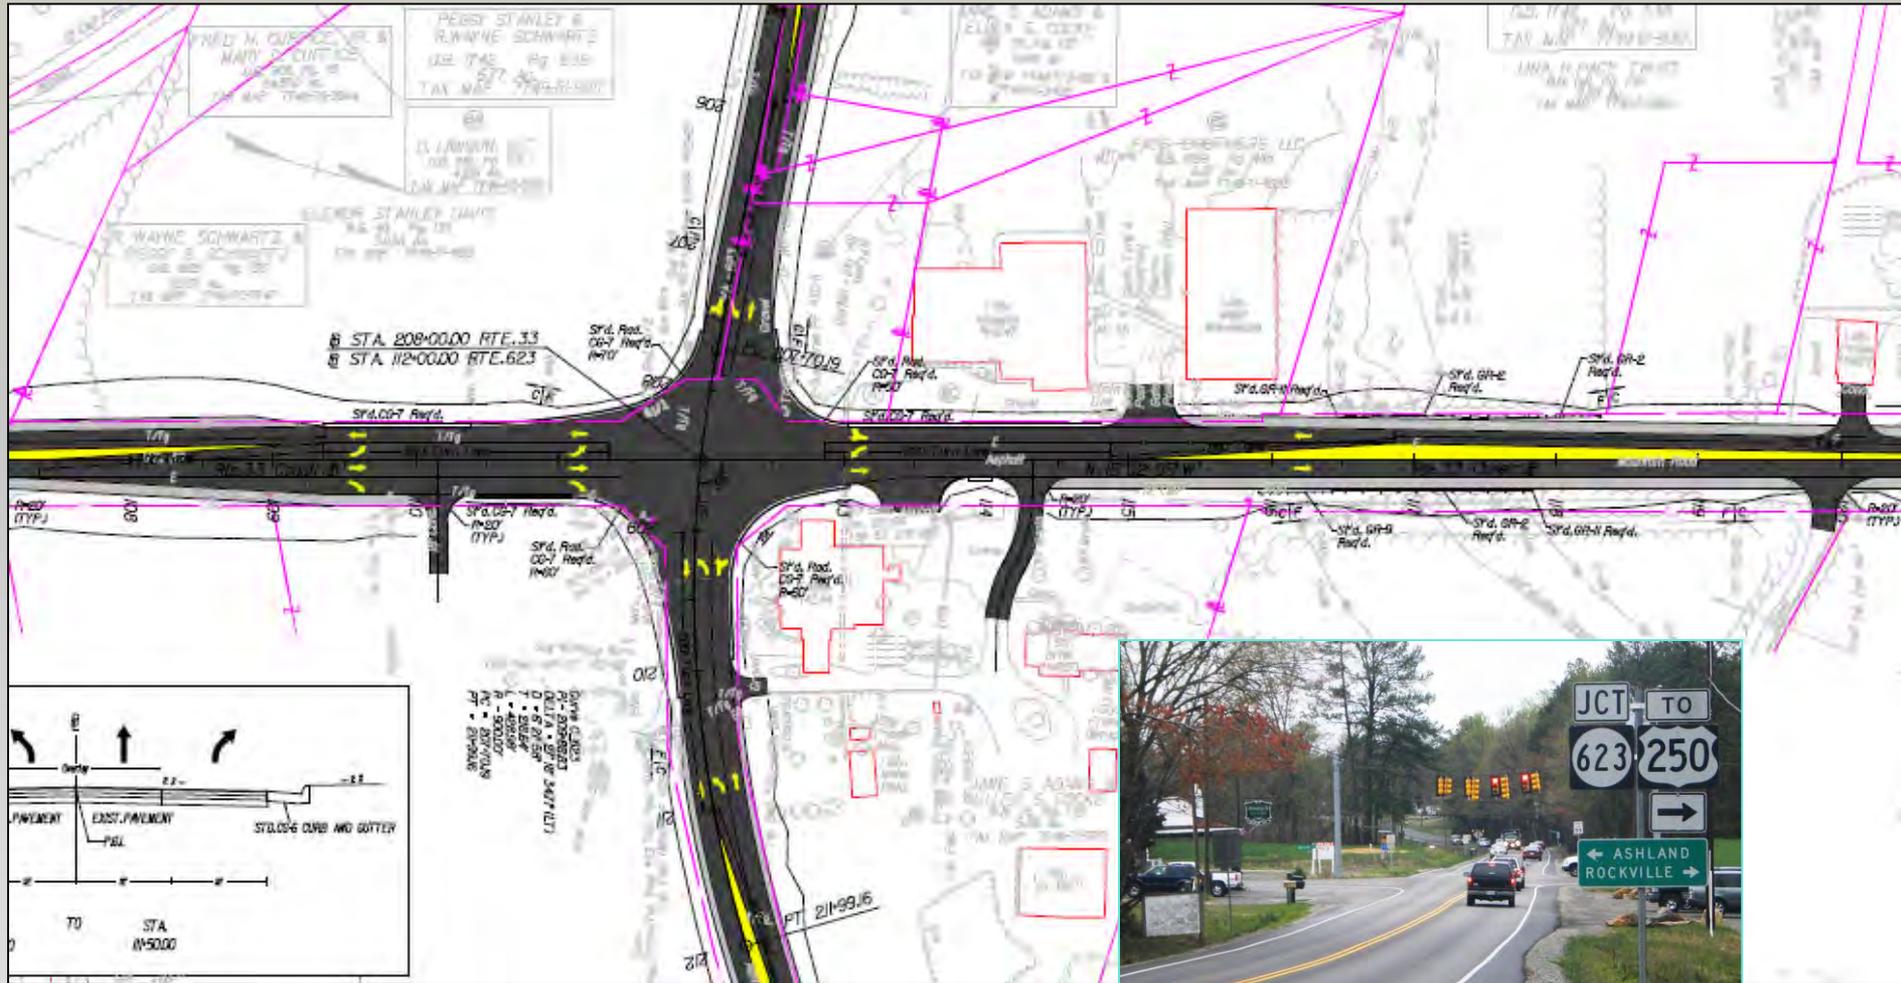


# 13 – Studley Rd. / Rural Point Rd (Roundabout)

## Design Phase – Sept. 16 Ad Date

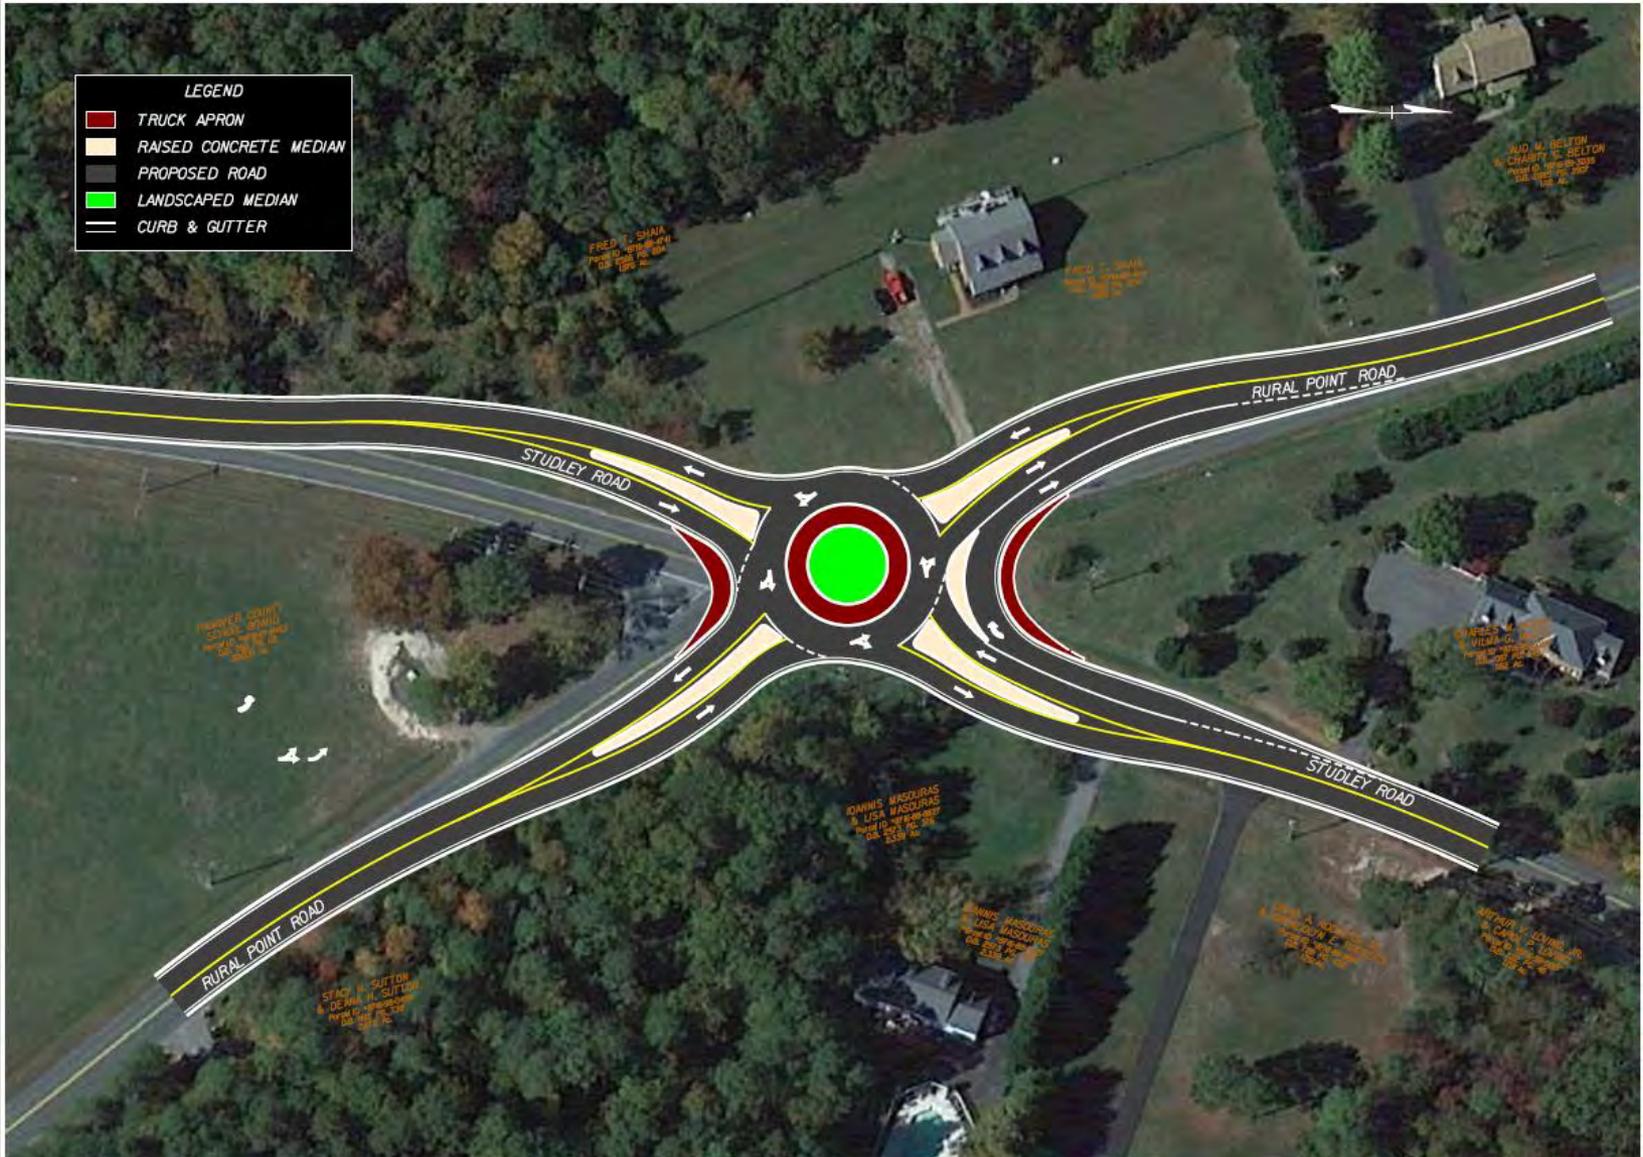



# 14 – E. Patrick Henry Rd. / Woodside Ln (Turn Lanes)

Design Phase – Sept. 2016 Ad Date

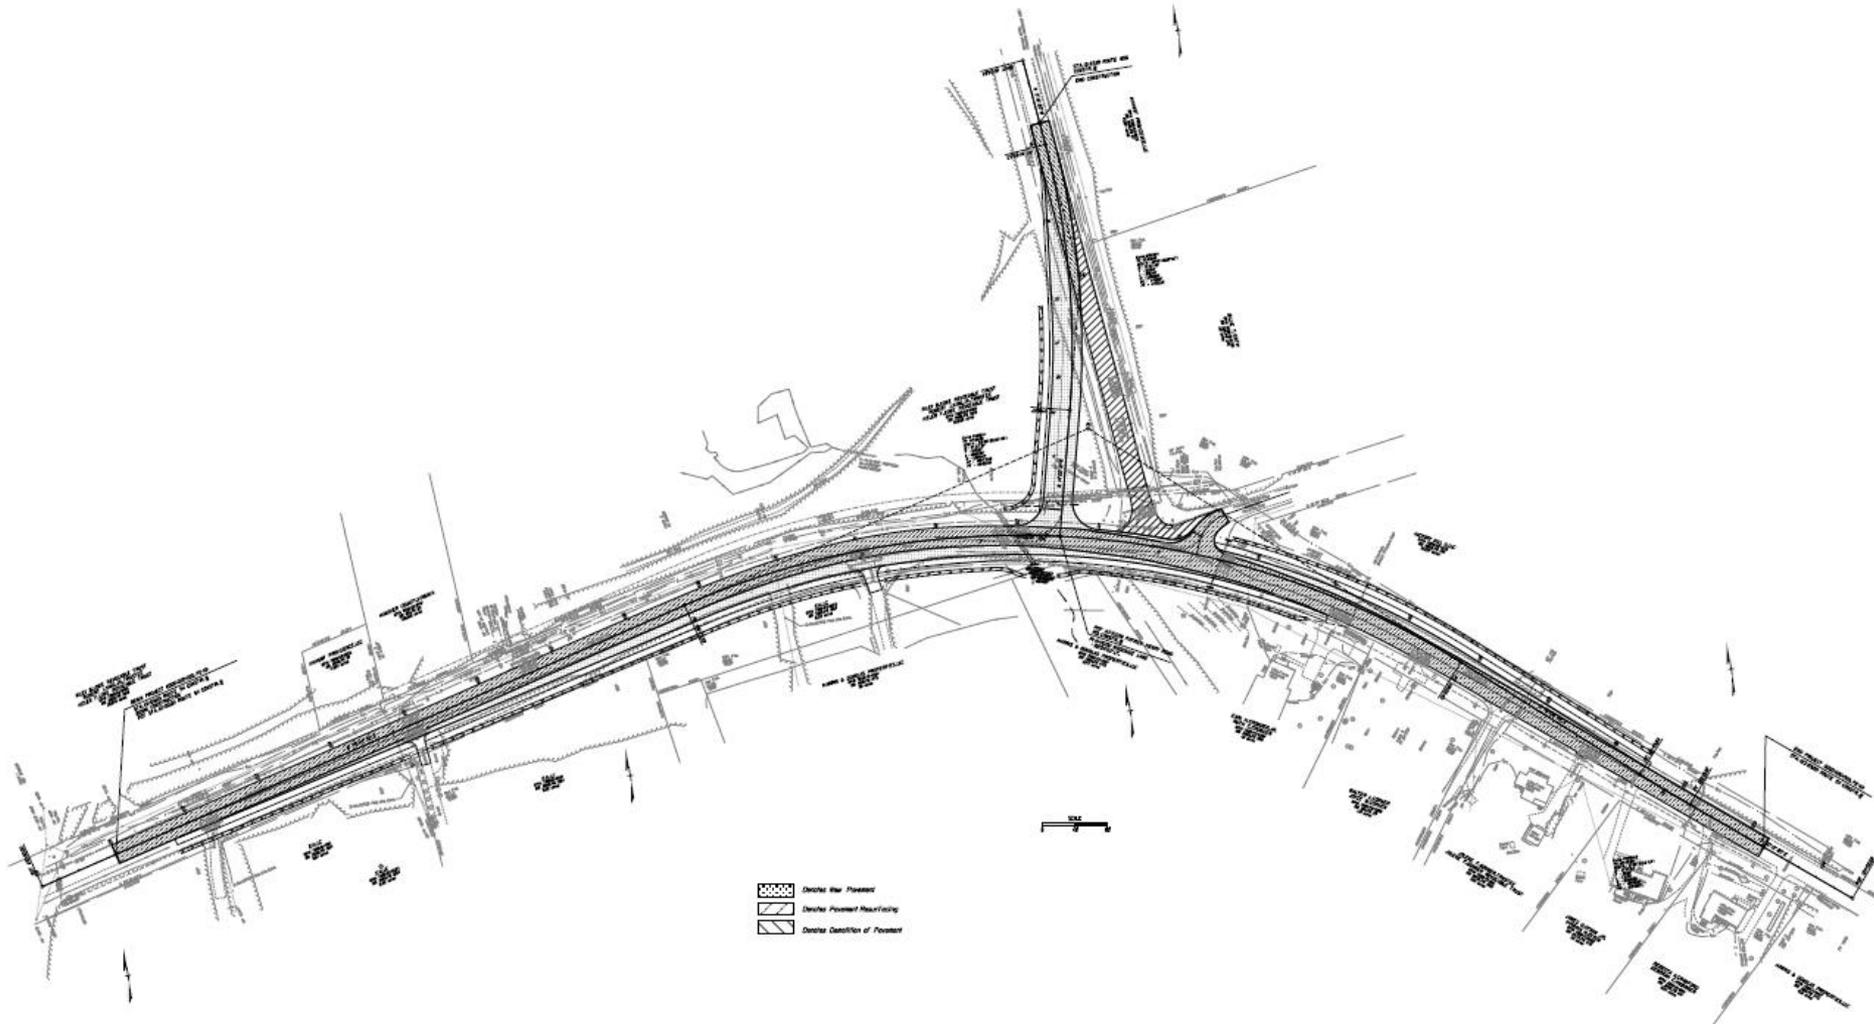

# 15 – Greenwood Rd. (Bridge & Approaches)

## Right-of-Way Phase – Sept. 2016 Ad Date

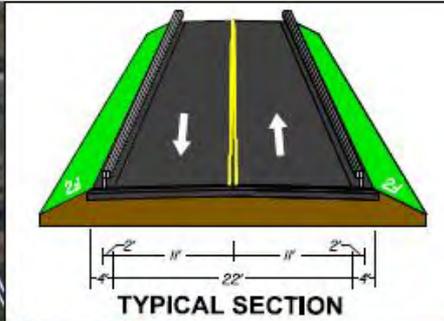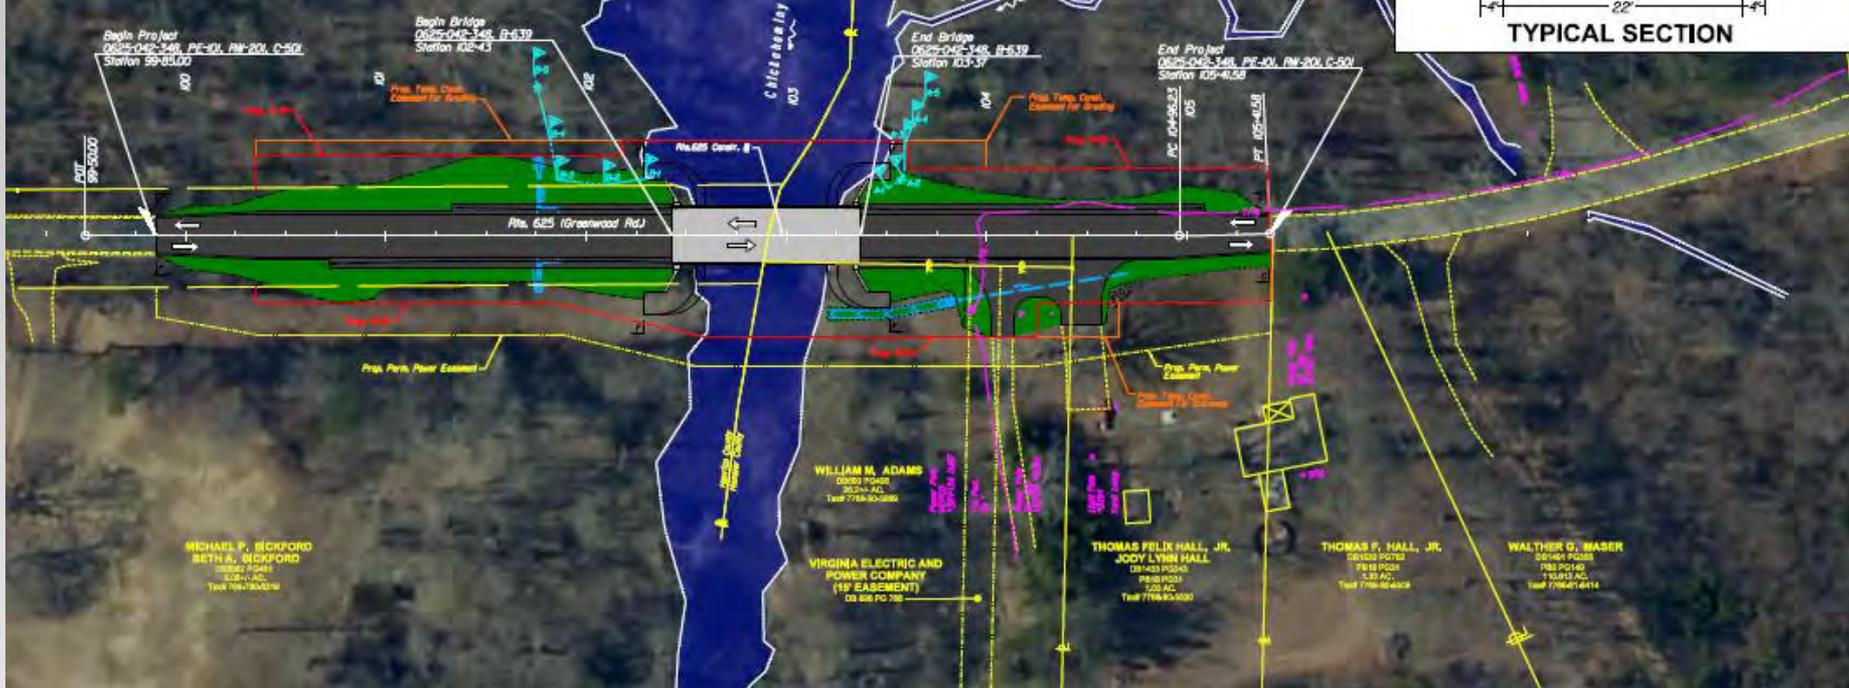

# 16 – Cedar Ln / U.S. Rt. 1 (Realignment)

Design Phase – Nov. 2016 Ad Date



# 17 – Atlee Rd. (Extension)


Right-of-Way Phase – Nov. 2016 Ad Date






# 18 – Creighton Rd / Cold Harbor Rd (Widening & Turn Lanes)

Design Phase – Ad Date TBD

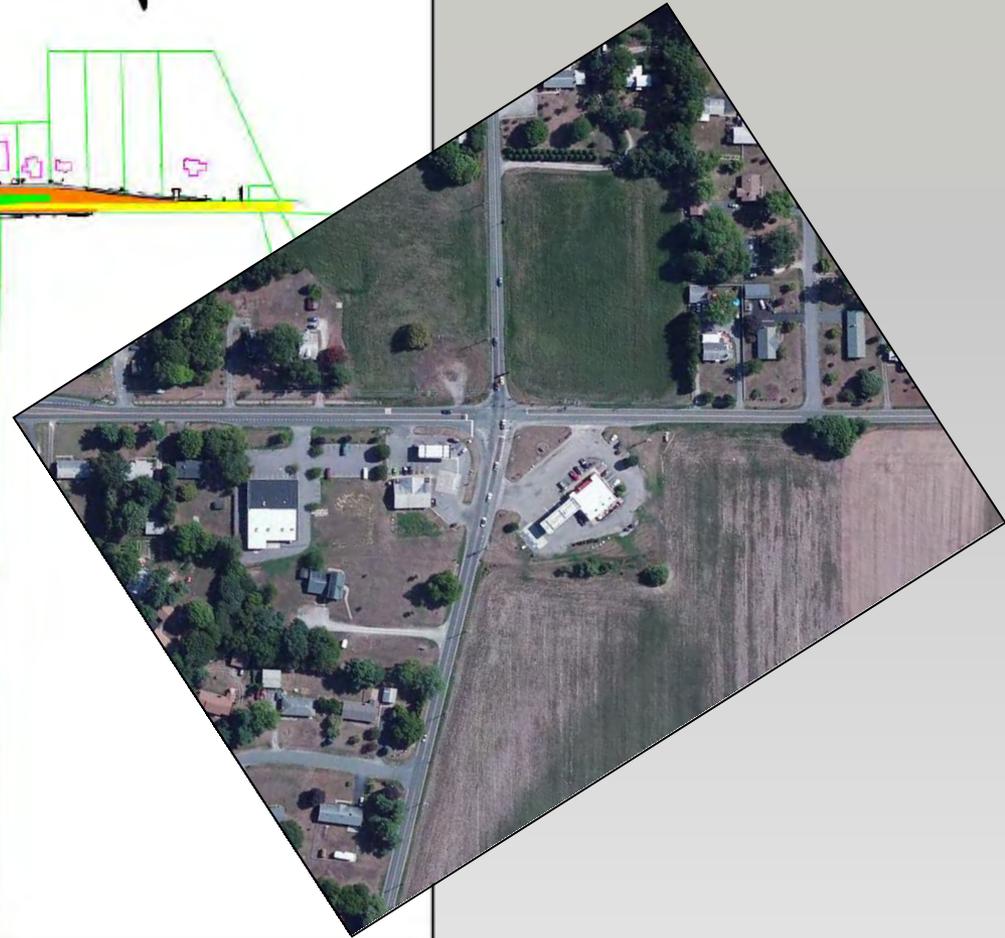

# 21 – Sliding Hill Rd (Widening)

Design Phase – (PE Only)

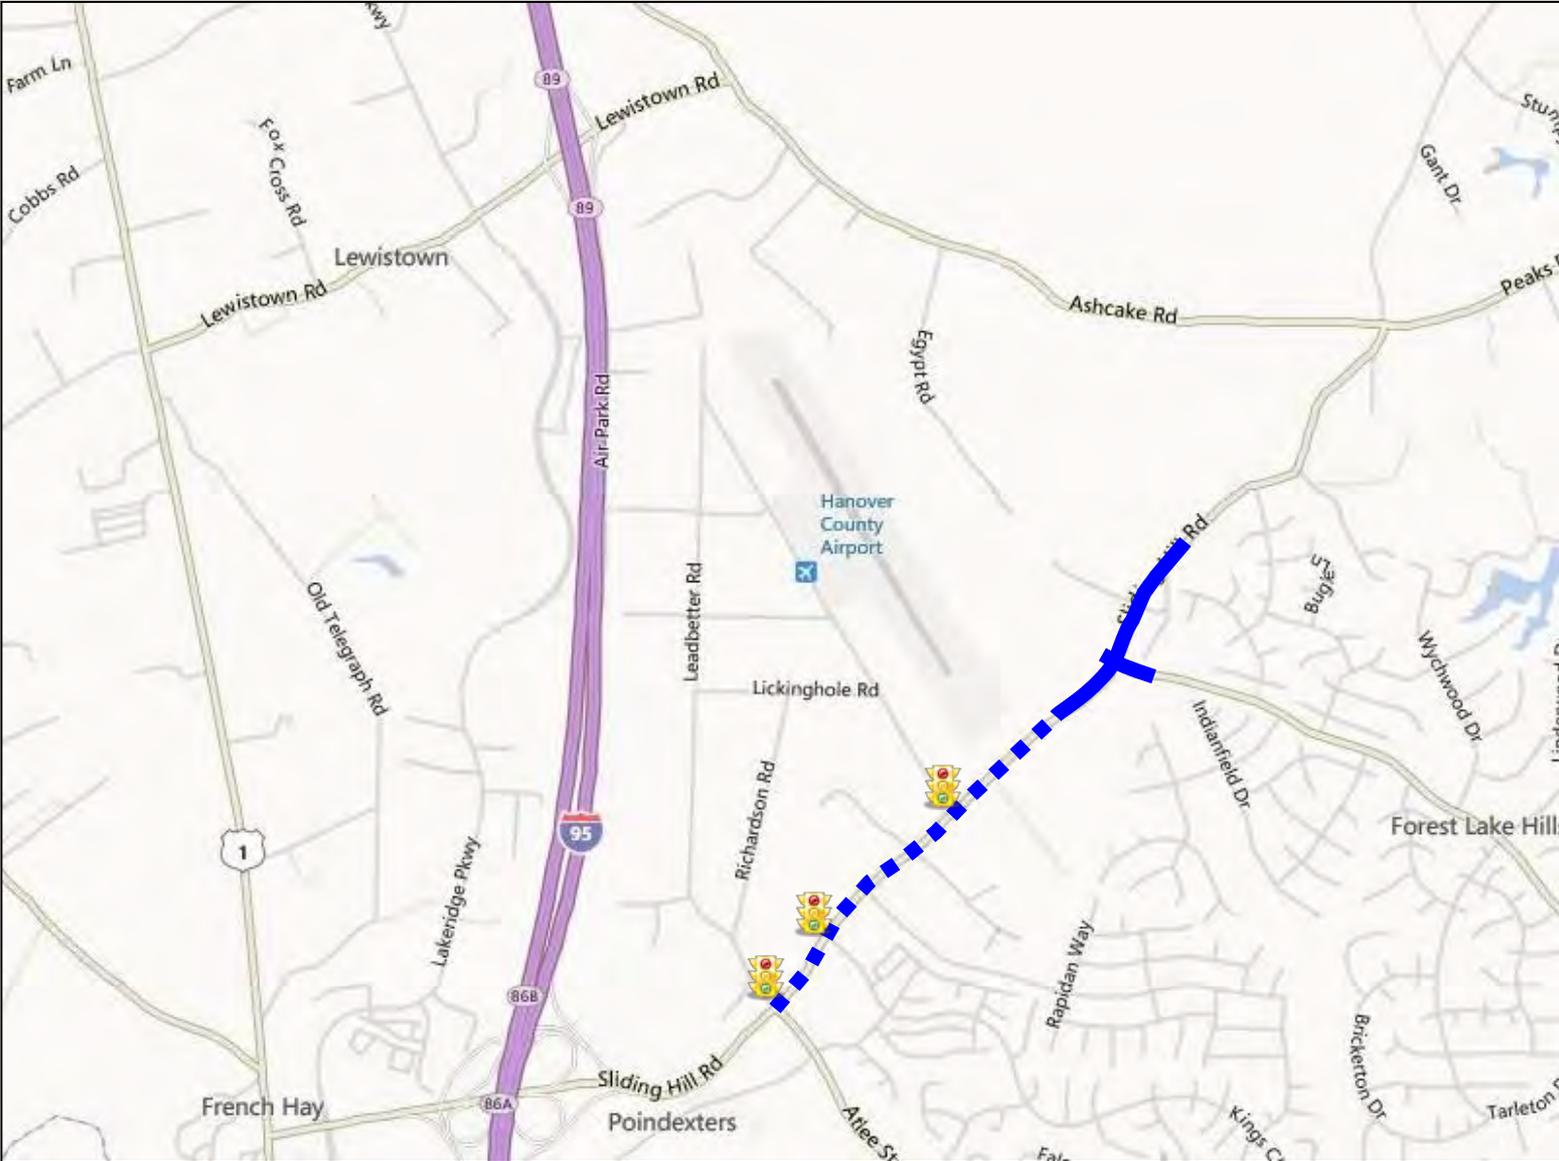

# 21 – Rt. 54 / I-95 Interchange

Analysis Phase – (PE Only)

